


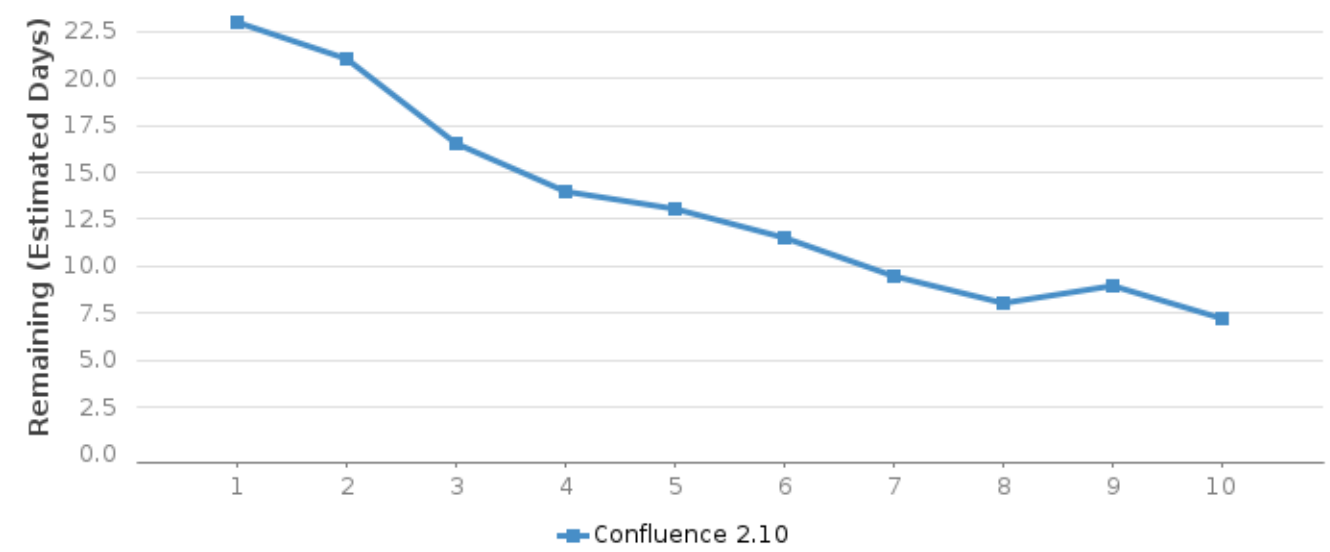
# Confluence 2.10 Release Dashboard

The Confluence development team always knows its status relative to plan. At the end of each week, the team updates the issues table below to show which issues were addressed and which ones carried over. The team also uses the {chart} macro to create a [burndown chart](#) showing how much work is left relative to how much time is left.

- [Edit this page and change one of the numbers in the chart](#). Save or preview the page to see your changes.
- [Edit this page and update the status one of the rows](#) by (like "quick-nav: selenium testing") by adding a  to the status column.


## Burndown chart

The following graph provides a rough status on the progress of the Confluence team.







## Rules for how to update the release dashboard:

Steps that need to be done at the end of an iteration

- Tasks that were finished get ticked off with a  and remain where they are.
- Tasks that have been started but not finished get moved to the next iteration. No estimates are changed, and in the comment field a text is added "carried over from previous x weeks".
- Tasks that were planned but not even started get moved to next iteration without comment.
- Velocity of previous iteration **may** be calculated and added, but only based on finished tasks, no matter how close unfinished tasks were to completion
- New unplanned work is added to the new iteration and marked in blue. cards that simply took longer than expected don't get any colour-coding.
- The "remaining estimated work" number from previous iteration remains unchanged.
- "Remaining estimated work" for the new iteration (including the backlog) is calculated based on the original estimates, and includes unplanned added work. So even a 2d-task that is considered 90% done will show up as 2d in the new iteration. The new iteration may exceed the previous velocity since we assume that there just remain 10%. But for the "remaining estimated work" the two days will be used.
- If the sum of all remaining work is larger than the original budget, some tasks at the end have to be declared as "won't fix" and greyed out. Their estimates are no longer counted for the remaining work.

2.10 is estimated to be a 3 month release, manned by a 2 person team (with one person doing part time bug fixing). Accounting for 1 week of sick or holiday leave, we have a feature budget of **14u** (11 iterations).

Iteration	Week 1: 30/JUL	Estimate	Remaining at very start of release cycle: 23
1	Discovery feature breakdown	1u	
	Remove SearchService	1u	
	Investigate/rework did-you-mean indexing	1u	
	Deploy RC1 to QA and Production	1u	
	Week 2: 6AUG	4u	Velocity: 4u. Remaining: 21

2	Make author filter work for external users (CONF-10769)	2u	✓
	<a href="#">Quick search by page title task breakdown</a>	1u	✓
	<a href="#">Respond to Did-You-Mean review feedback</a>	1u	✓
	Add author filter to people directory	1u	Decided to discontinue work on card after 0.5u investigation.
	<b>Week 3: 13/AUG</b>	<b>4u</b>	<b>Velocity: 5u. Remaining: 16.5u</b>
3	Make author filter work for hosted	2u	✓
	<a href="#">Fix archiva with James</a>	0.5u	✓
	<a href="#">Discovery planning</a>		✓
	<a href="#">Code reviews</a>		✓
	<b>Week 4: 20/AUG</b>	<b>4.5u</b>	<b>Velocity: 2.5u. Remaining: 14u</b>
4	quick-search-by-title: Add lucene index fields	1u	
	<b>Week 5: 27/AUG</b>	<b>1u</b>	<b>Velocity: 1u. Remaining: 13u</b>
	did-you-mean: merge to trunk	0.5u	✓
	did-you-mean: run clover and add tests	1u	✓
	<b>Week 6: 3/SEP</b>	<b>1.5u</b>	<b>Velocity: 1.5u. Remaining: 11.5u</b>
	quick-search-by-title: backend	2u	✓ Carried over twice from previous iteration, took longer than expected
	<b>Week 7: 10/SEP</b>	<b>2u</b>	<b>Velocity: 2u. Remaining: 9.5u</b>
	quick-search-by-title: JSON	0.5u	✓ Carried over from previous iteration
	quick-search-by-title: UI Integration	1u	✓ Carried over from previous iteration
	search-visuals: clean up display of individual results	2u	✓
	<b>Week 8: 10/SEP</b>	<b>3.5u</b>	<b>Velocity: 3.5u. Remaining: 8u</b>
	<a href="#">quick-nav: bug fixes (unicode, themes, highlighting)</a>	1u	✓
	<b>Week 9: 17/SEP</b>	<b>1u</b>	<b>Velocity: 1u. Remaining: 11u</b>
	<a href="#">quick-nav: selenium testing</a>	1u	
	search-visuals: Add people thumbnails to search results	1u	
	<b>Week 10: 24/SEP</b>	<b>2u</b>	
	<a href="#">did-you-mean: indexing issues (CONF-12943)</a>	1u	
	<b>Week 11: 6/OCT</b>	<b>1u</b>	
	quick-search-by-title: Advanced JS component <ul style="list-style-type: none"> <li>• IE bug (CONF-13158)</li> <li>• density and organisation</li> <li>• Caching issues</li> </ul>	3u	
	<a href="#">quick-nav: performance testing</a>	1u	
	<a href="#">quick-nav: Timouts (CONF-13062)</a>	1u	
	<b>Week 12: 13/OCT</b>	<b>4u</b>	
	OpenSearch plugin (advertisement only)	0.5u	
	<a href="#">quick-nav: Document for custom layouts (CONF-13073)</a>	0.25u	
	<b>Week 13: 20/OCT</b>	<b>0.75u</b>	

## Dropped from release

<a href="#">quick-nav: relevancy: boost by favourites</a>	2u	(not counted for remaining estimate, since originally unplanned and not in current plan anymore)
search-visuals: Adjust number of results per page	1u	
Change default space content	0.5u	
<a href="#">did-you-mean: auto-enable for english customers (CONF-13209)</a>	1u	



**Warning: Sample Content**

This is sample content that comes included with Confluence for the purposes of demonstrating how the product can be used.
